

EVNet Sentinel: Project Planning

Network Diagram, Critical Path, and Gantt Chart

Group 1

September 22, 2026

1. Project Task Details


To establish the critical path and network diagrams efficiently, task durations have been logically estimated based on the EVNet Sentinel SRS and DFD.

ID	Task Name	Duration (Days)	Predecessors
A	Load Datasets	3	-
B	Parse & Scale	5	A
C	Mask PII & Feature Eng	6	B
D	Static Models	12	C
E	Online Adaptive Model	15	C
F	Train & Tune	8	D, E
G	Classification Reports	5	F
H	Traffic Simulator	8	C
I	Synthetic Injector	7	H
J	FastAPI Backend	10	G, I
K	Dashboard UI & Metrics	10	J
L	Live Alerts & Matrices	8	K
M	Simulation Controls	7	K
N	Anomaly Investigation	7	K
O	E2E Integration	12	L, M, N
P	Final Evaluation	6	O

2. Network Diagram and Critical Path

The highlighted red path indicates the Critical Path: **A** → **B** → **C** → **E** → **F** → **G** → **J** → **K** → **L** → **O** → **P** (Total: 88 Days ≈ 4 Months). Each node follows the standard PERT format:

Early Start (ES)	Task ID	Early Finish (EF)
Task Name		
Latest Start (LS)	Duration	Latest Finish (LF)

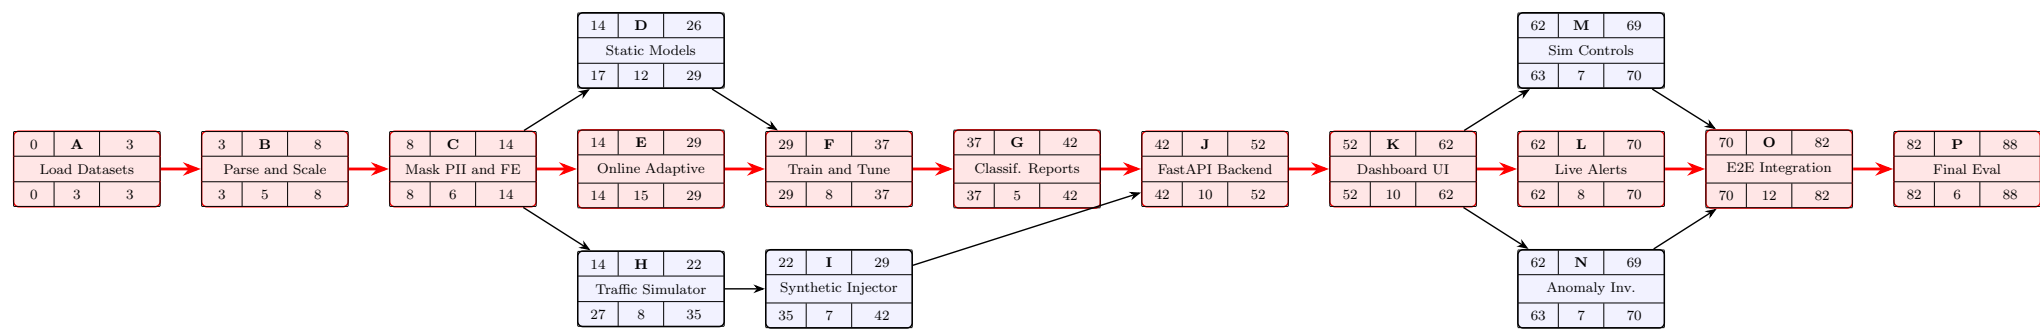

3. Gantt Chart

